


# BUILDING PROJECT JULY UPDATE

The following is an update of the project as at the end of July 2018

## FINANCIALS

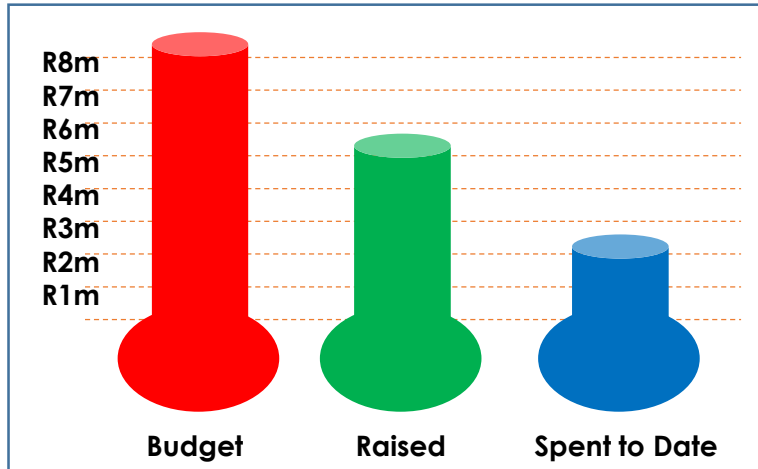

**Budget** – R8,675,000

**Funds Raised** – R5,700,000

**Spent to Date** – R2,600,000

## BUILDINGS

- **Training Centre**
  - Electricity commenced
  - Plastering completed
  - Ceilings in progress
  - Painting commenced
- **Pre-School**
  - Bricklaying at roof height
  - Roof trusses ordered
  - Electricity to start
  - Covered walkway in progress



[MORE PICTURES](#)

PROJECT % COMPLETION IS 42% | PROJECT COMPLETION DATE – 14 DECEMBER 2018
